

# **RETAINING WALL - MODULAR UNIT REINFORCED EARTH TENSAR GEOGRID REINFORCEMENT**

**Final Report  
For  
HR-549**

**January 1998**

**Project Development Division**



**Iowa Department  
of Transportation**

Final Report  
for  
HR-549

RETAINING WALL - MODULAR UNIT REINFORCED EARTH  
TENSAR GEOGRID REINFORCEMENT

BLAIRS FERRY ROAD/LINDALE DRIVE INTERSECTION  
RECONSTRUCTION PROJECT  
MARION, IOWA  
M-MG-0820(4)--8X-57

City of Marion  
Engineering Department

By  
Maryann Shinrock  
Assistant City Engineer  
PH: 319-373-9422  
City of Marion  
195 35th Street  
Marion, Iowa 52302

and

Mohammad Mujeeb  
Materials Technician 4  
PH: 515-239-1086  
FAX: 515-239-1092  
Materials - Research  
Project Development Division  
Iowa Department of Transportation  
Ames, Iowa 50010

January 1998

## TECHNICAL REPORT TITLE PAGE

---

**1. REPORT NO.**

HR-549

**2. REPORT DATE**

January 1998

---

**3. TITLE AND SUBTITLE**

Retaining Wall - Modular Unit  
Reinforced Earth Tensar Geogrid  
Reinforcement

**4. TYPE OF REPORT & PERIOD COVERED**

Final Report, 6-92 to 1-98

---

**5. AUTHOR(S)**

Maryann Shinrock

Mohammad Mujeeb

**6. PERFORMING ORGANIZATION ADDRESS**

City of Marion  
195 35th Street  
Marion, Iowa 52302

Iowa Department of Transportation  
Materials Department  
800 Lincoln Way  
Ames, Iowa 50010

---

**7. ACKNOWLEDGMENT OF COOPERATING ORGANIZATIONS**

---

**8. ABSTRACT**

This research, initiated in October 1992, was located at the intersection of Blairs Ferry Road and Lindale Drive in the City of Marion. The wall is located on the southeast corner of the intersection. Reinforced retaining wall construction started with a five inch base of roadstone with one inch of sand for leveling purposes. One and one-half to two feet of one inch clean stone was placed behind the blocks. A four inch perforated plastic pipe was placed approximately nine inches from the bottom of the one inch clean stone. The Tenswal, tensar geogrid was placed at every third layer. Openings in the Tenswal are hooked over plastic dowels in the blocks. The tenswal reaches from the face of the wall back 5' to 8'. The cost for constructing this wall was \$124,400. The wall has performed well for the past five years. The wall improves the aesthetics of a high traffic volume intersection of an urban area. Many positive comments have been received by the city regarding its appearance. The City of Marion has been pleased with the wall and has used this type of wall on subsequent projects.

---

**9. KEY WORDS**

Reinforcement  
Tenswal  
Retaining wall  
Geogrid

**10. NO. OF PAGES**

11

## TABLE OF CONTENTS

	Page
Introduction .....	1
Construction .....	1
Monitoring .....	2
Conclusion .....	3
Appendix	
Appendix A - Step-by-Step Construction of the Wall .....	4

## DISCLAIMER

The contents of this report reflect the views of the authors and do not necessarily reflect the official views of the Iowa Department of Transportation. This report does not constitute any standard, specification or regulation.

## **INTRODUCTION**

This is the final report on the construction and performance of a Tensar fabric-reinforced soil retaining wall with modular concrete block facing units constructed in the City of Marion.

The modular retaining wall was investigated originally as an alternative to a conventional cast-in place reinforced concrete retaining wall to support a 10 foot high embankment. Preliminary cost estimates determined approximately equal costs for both. The modular design was selected based upon aesthetic appearance in the high traffic volume intersection.

Analysis and design was performed by Ament Engineering, Inc. of Cedar Rapids, Iowa. The design analysis determined the spacing and strength of geogrid necessary to resist the lateral earth pressures and surcharge loads of the existing soils. Technical support during design and construction was provided by Kings Material, Inc., Contech Construction Products and Terracon Consultants.

The wall was constructed as a part of an intersection reconstruction project, M-MG-0820(4)--8X-57, in 1993. The prime contractor was Rathje Construction Company of Marion, Iowa; subcontractor constructing the retaining wall was Anne Duffield Construction, Inc. of Cedar Rapids, Iowa. The project location is the intersection of Blairs Ferry Road and Lindale Drive in the City of Marion. The wall is located on the southeast corner of the intersection.

In conjunction with this project, three individual walls were constructed. Two were approximately 24 inches in exposed height and did not require Tensar reinforcement. This report deals primarily with the large Tensar-reinforced wall.

## **CONSTRUCTION**

Excavation of the existing soil was made to the bottom of the footing elevation. Existing soils were proof rolled for stability testing. The 6" x 36" wall footing material was a five inch thickness of 1 inch granular material topped with 1 inch of fill sand for grading and leveling purposes. All base materials were compacted.

Modular block units were set and checked for position and levelness. Upon completion of the first row of block, the block unit openings were filled with 3/8 inch minus aggregate and hand tamped with hammers. Compactive efforts within the block units were limited by the size of the openings.

A corrugated polyethylene drain tile was installed behind the base row of block to facilitate drainage. The tile was discharged into a storm sewer. Backfill behind the wall was placed as each row of block was installed. A free draining material (1 inch clean aggregate) was placed immediately behind the wall. Backfill over the geogrid was a 3/4 inch minus aggregate which was compacted.

Successive rows of block were anchored with fiberglass dowels,  $\frac{1}{2}$ " x  $9\frac{1}{4}$ ", inserted into the head sections of each block from the previous row to prevent horizontal shifting of the blocks. Each successive row of blocks straddled two block units from the row underneath and were set back one inch. The ends of each wall were bent or curved into the backfill for visual purposes.

Tensar geogrid fabric was placed at the elevations and lengths specified. The end of the grid was looped over the block units dowels and the fabric was stretched tight behind the wall. In curved sections, geogrid sheets were overlapped in order to keep their alignment relatively perpendicular to the face of the wall.

Cap units topped the upper row of standard blocks. These units have solid tops with drilled holes for dowels in their underside. One foot of native topsoil was placed on top of the completed backfill to minimize surface water infiltration behind the wall.

A wooden fence was constructed on top of the embankment with posts anchored approximately 30 inches behind the wall cap units.

The majority of the construction was performed with hand labor. Each block unit must be individually set and checked for position and levelness. Survey for elevations and alignment of the wall base was critical.

Appendix A shows a typical cross-section of the wall and photograph of the step-by-step construction of the wall.

## **MONITORING**

Reference points for monitoring horizontal and vertical displacement of the large retaining wall were established. Biannual checks of elevations and measurements were made in a three year period. Overall visual inspections were also performed.

No significant irregularities have been noted in the vertical or horizontal alignment of each row or vertical projection during this inspection period. The offset of each successive row of blocks appears to be maintained. No leakage between block units or separation of block units is apparent. Some drainage through the blocks down the face of the wall is visible after extended periods of precipitation, however, most drainage is through the backfill behind the wall into the base drintile.

One concern noted in the first year monitoring report was vegetative growth occurring between some block units. An annual application of weed killer to the face of the wall has eliminated this problem.

## **CONCLUSION**

Final cost of the completed large wall was \$124,400. While there were no significant (estimated) cost savings between this type of construction and conventional cast-in-place construction, the aesthetic effects have a significant value.

The wall has performed well in the past five years. Its location is in a high traffic volume intersection of an urban area which allows great visibility. Many positive comments have been received by the City regarding its appearance.

The City of Marion is pleased with the construction and has used this type of wall construction on other projects.

Appendix A  
Step-by-Step Construction of the Wall



42" HIGH WOOD FENCE  
(POST SPACING = 8'-0");  
POST ENCASEMENT DEPTH  
= 2.67 FEET (CONTRACTOR  
SHALL MINIMIZE DAMAGE TO  
ANY GEOGRID LAYERS THAT  
ARE PENETRATED BY POSTS  
AND ENCASEMENT)

PLACE A ONE-FOOT LAYER (APPROX.)  
OF NATIVE SOIL OR LOW-PERMEABILITY  
SOIL TO MINIMIZE SURFACE WATER  
INFILTRATION

WALL SETBACK =  
1" PER 8" RISE

EXISTING GROUND LINE

4:1 SLOPE (MAXIMUM)

CAP UNIT

3/8" granular fill

MODULAR CONCRETE  
FACING UNITS

GEOGRIDS  
(TYP.)

HEIGHT (VARIES)  
HEIGHT MEASURED FOR  
PAYMENT (ITEM NO. 53)

PAYMENT LIMIT LINE \*

REINFORCED WALL FILL ZONE

3/4" granular fill / sand

1" clean aggregate

SUBDRAIN

PAYMENT LIMIT LINE \*

LEVELING  
PAD

5" roadstone / 1" sand

FOUNDATION SOIL ZONE


\*FOR CLASS 23  
EXCAVATION

GEOGRID LENGTH  
(VARIES WITH WALL HEIGHT)  
(LENGTH MEASURED FROM FRONT FACE)

PAYMENT LIMIT LINE \*

RETAINED BACKFILL ZONE

# TYPICAL SECTION OF RETAINING WALL

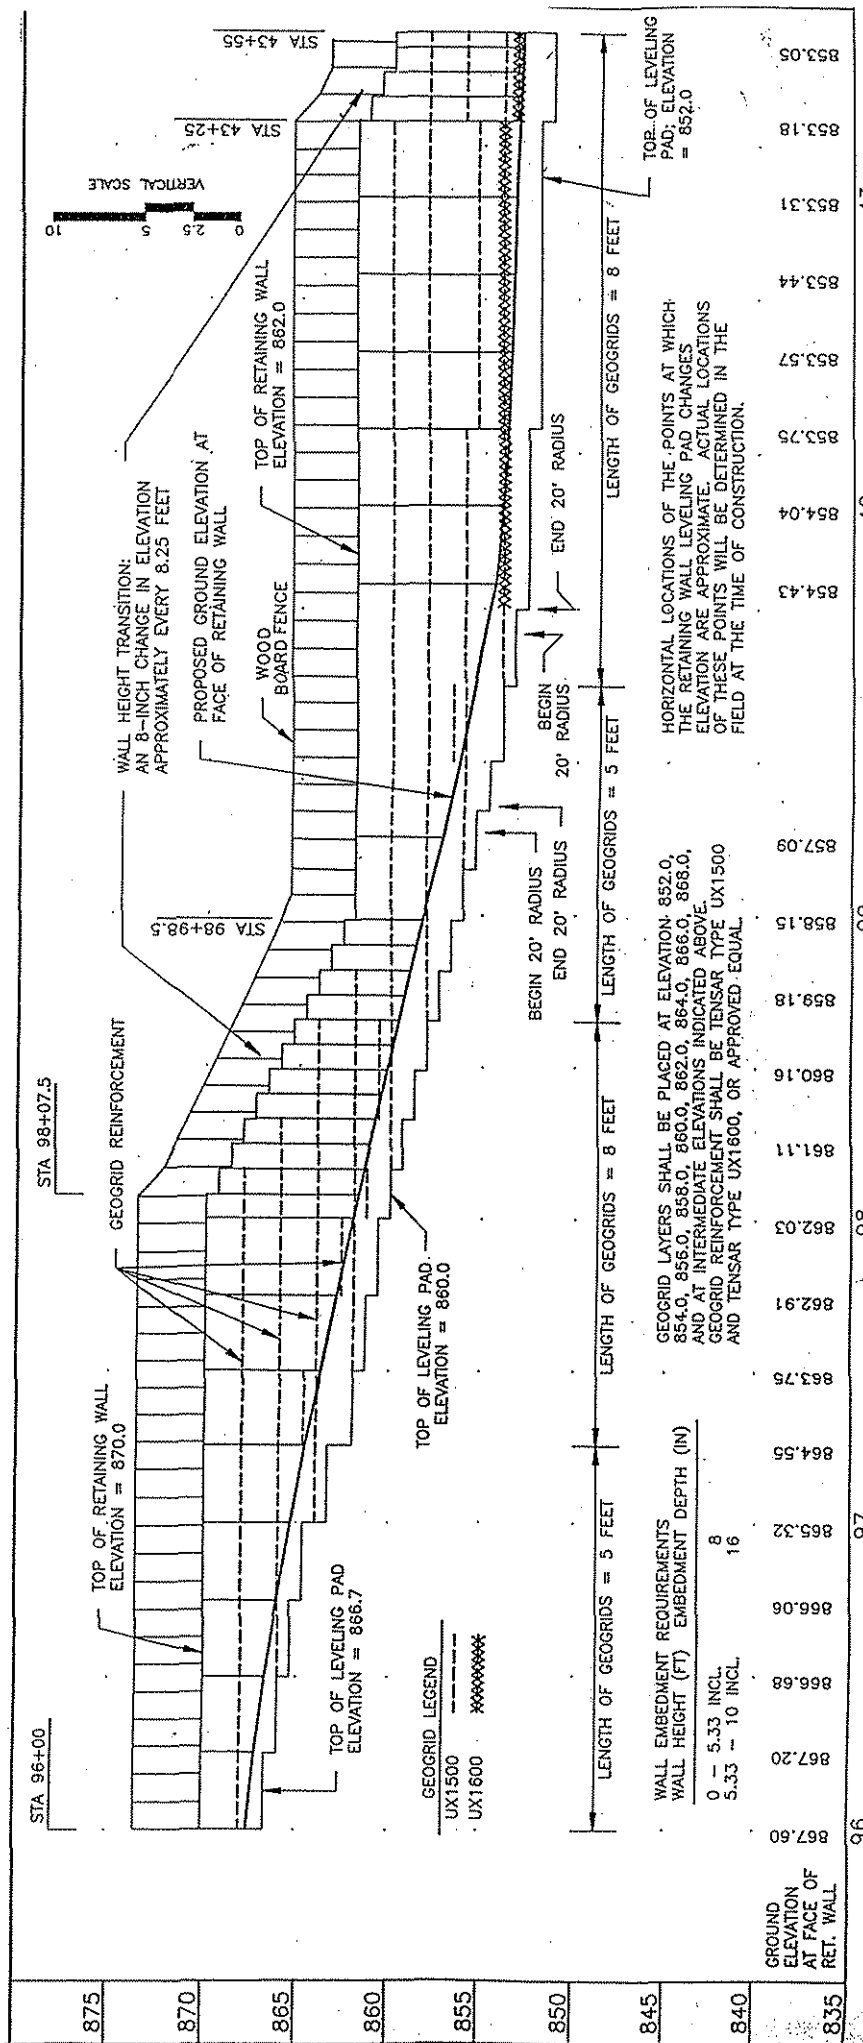

BLOCK UNIT DATA

**GENERAL INFORMATION:**



- Compressive Strength ..... 3000 psi
- Absorption Rate ..... 6 to 8 lbs/ft<sup>3</sup>
- Composition ..... High Strength, High Density Concrete


**STANDARD UNIT:**

- Weight ..... 94 lbs. .... (42.64 kg)\*\*
- Size ..... 8"H x 18"W x 24"D ..... (2032m H x 457m W x 6096m D)
- Exposed Face Area ..... 1 Square Foot (8"x18")... .093 Square

## CAP UNIT:

- Weight ..... 78 lbs..... (35.38 kg)\*\*
- Size ..... 8"H x 18"W x 12"D ..... (2032m H x .4572m W x .3048m D)\*\*
- Exposed Face Area..... 1 Square Foot (8"x18").. .093 Square Meters (.2032m x .4572m)



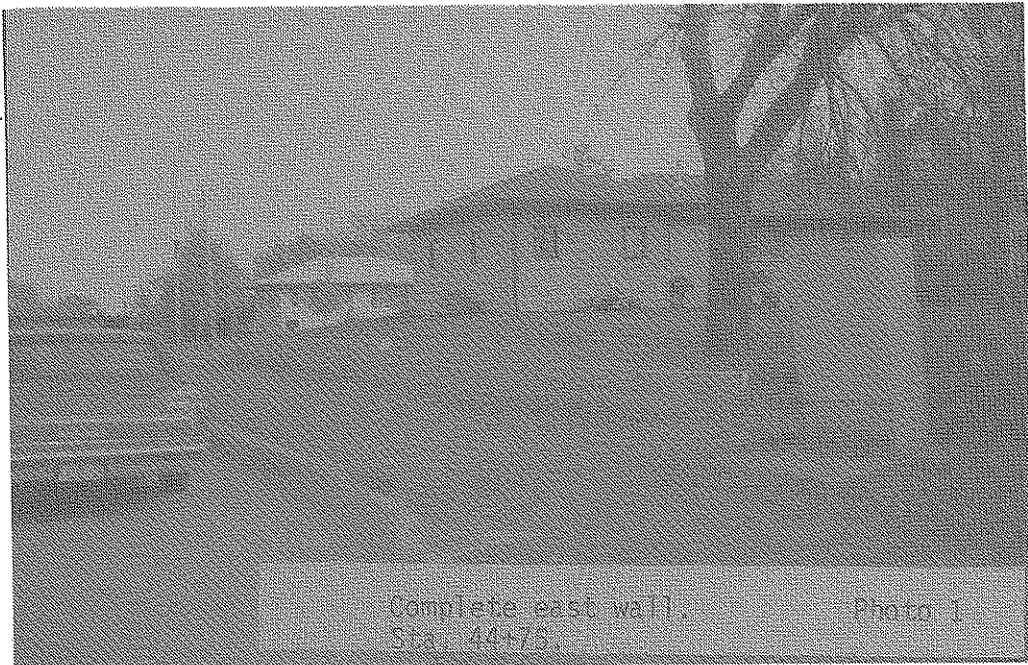


Complete east wall.  
Sta. 44+75.

Photo 1



Completed west wall.  
Sta. 37+00.


Photo 2

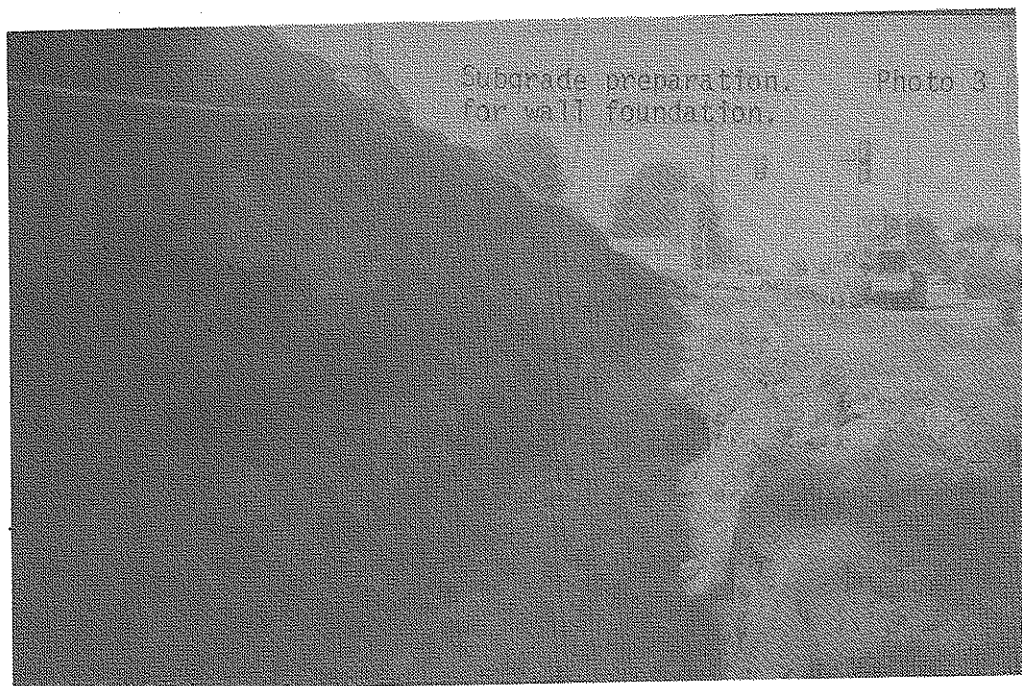

Subgrade preparation.  
for wall foundation.

Photo 3



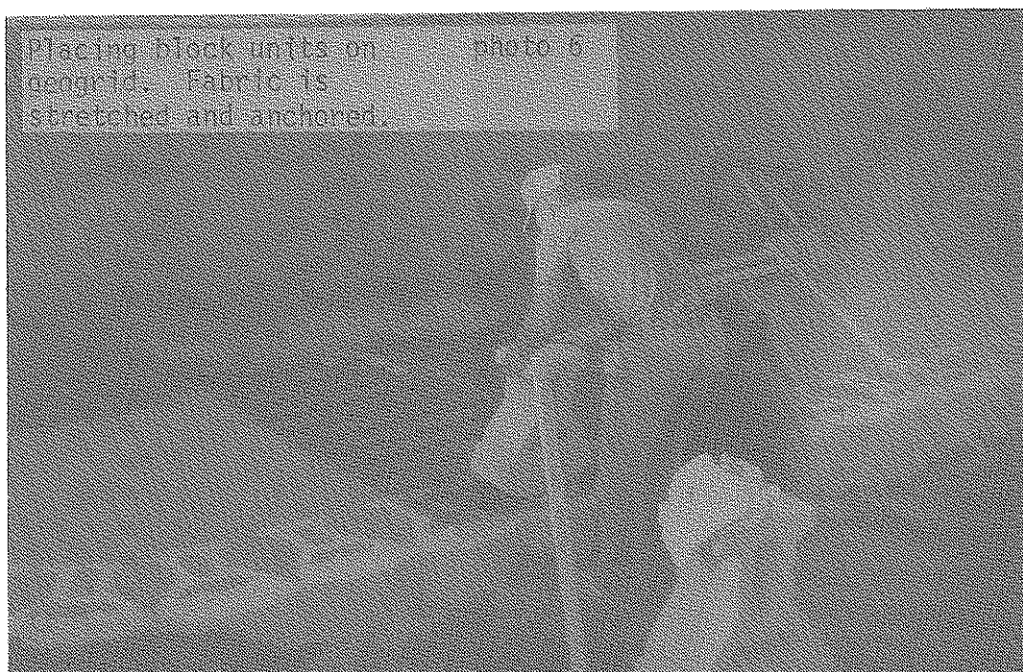


Placing geogrid.  
Fabric is stretched and  
anchored.

Photo 7




Overlap of geogrid  
at wall end anchorage.

Photo 8

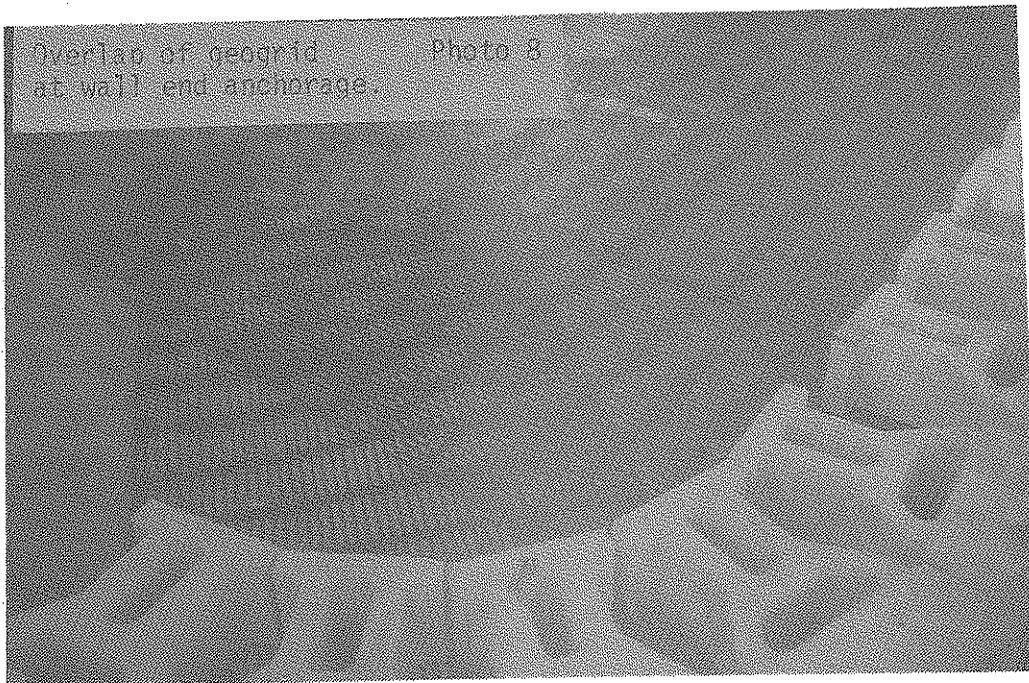


Backfill, 1" clean  
at drain tile. Sand select  
over geogrid.

Photo 9

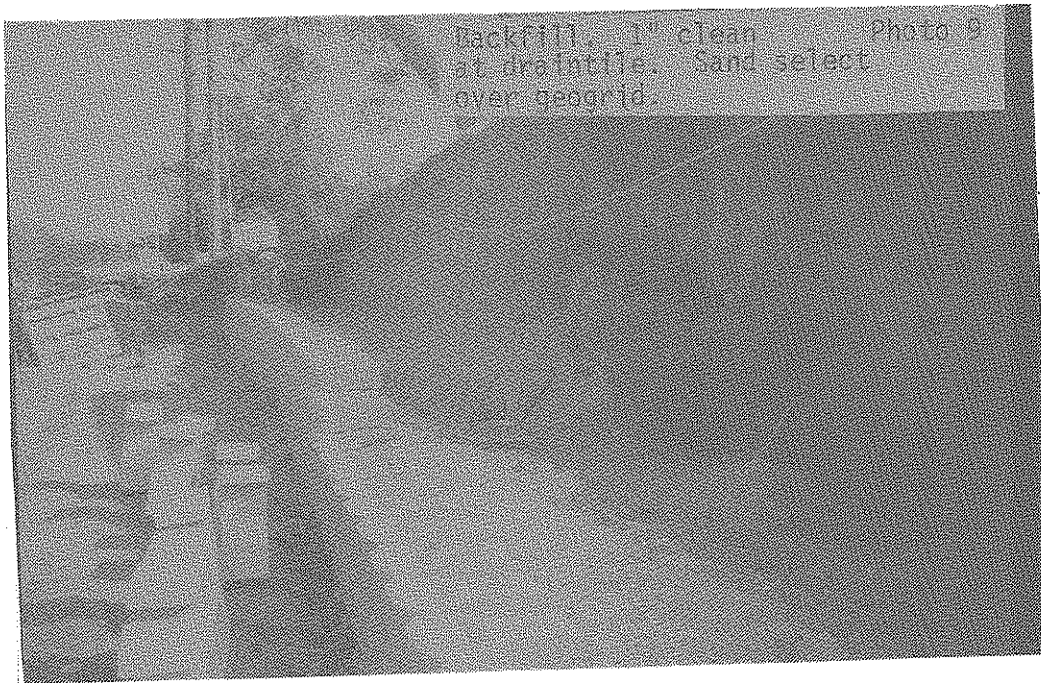




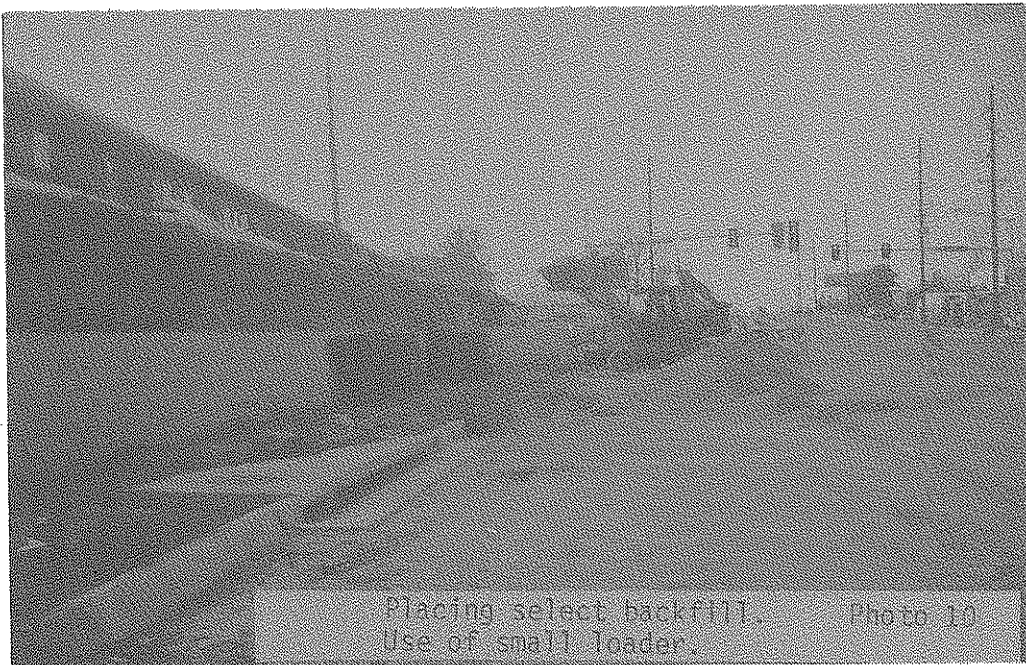


Placing select backfill.  
Use of small loader.

Photo 10

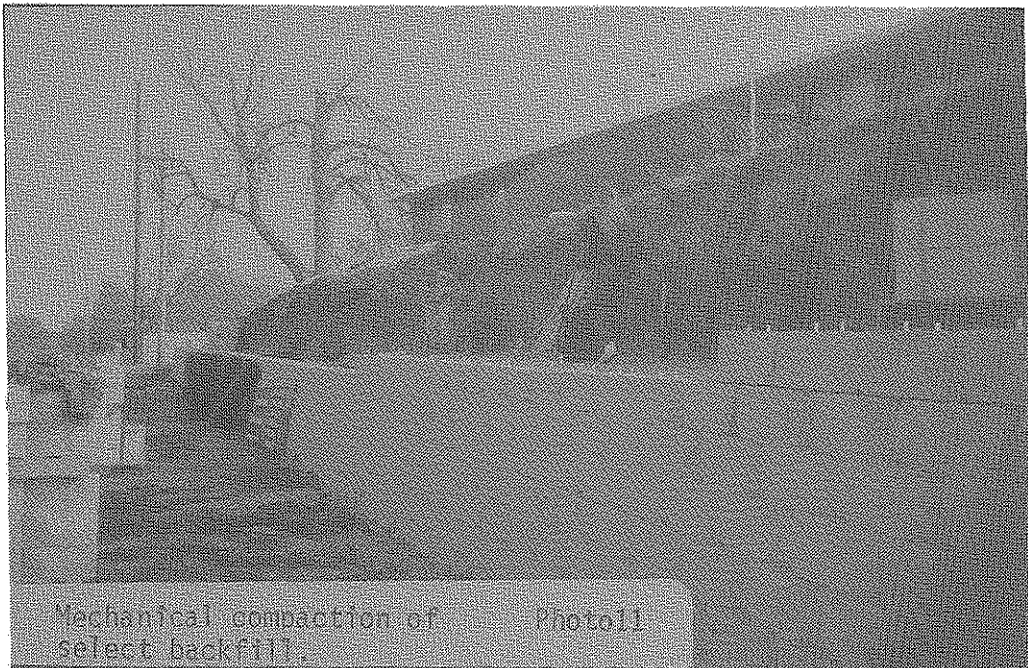


Mechanical compaction of  
select backfill.

Photo 11

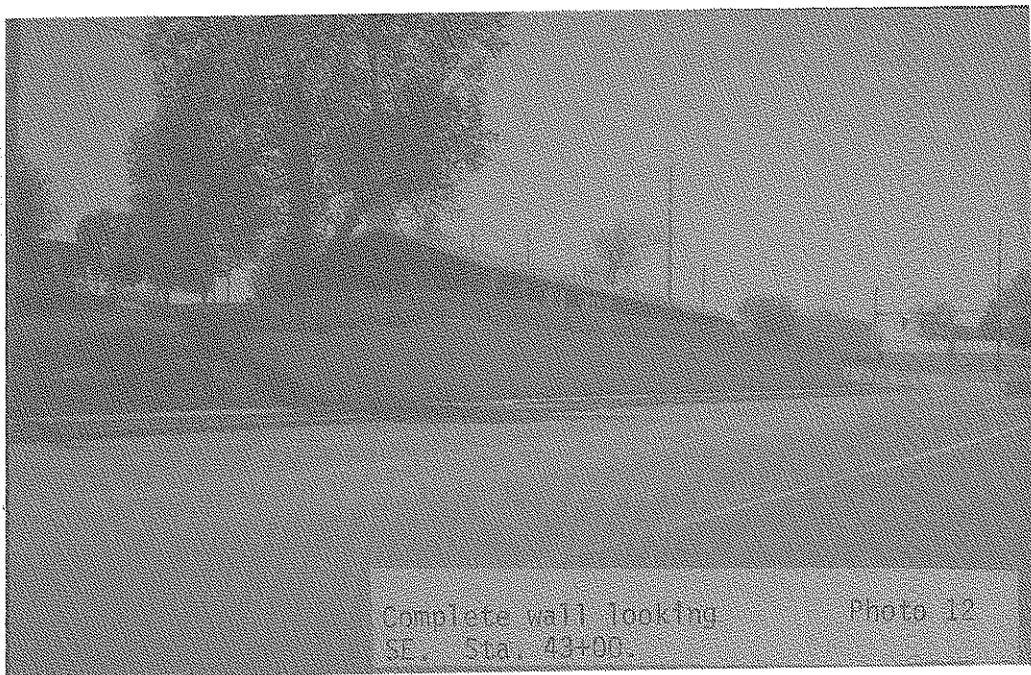

Complete wall looking  
SE, Sta. 43+00.

Photo 12

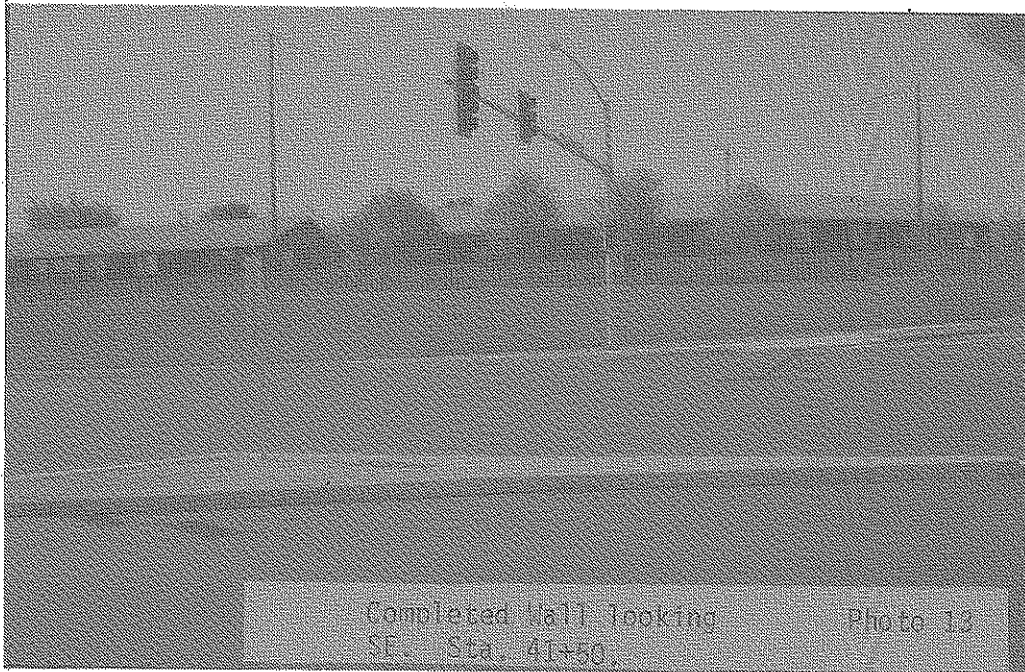

Completed Wall looking  
SE. Sta. 41+50.

Photo 13
